



Downtown Brampton Interim Phase 1 Works

Community Update
January 2021

What are we doing and why?


- Region of Peel and City of Brampton are coordinating interim water and wastewater infrastructure and road works in Downtown Brampton
- Originally planned to be replaced as part of Downtown Reimagined, which was placed on hold in December 2018, pending an implementation plan for the various projects in the downtown including consideration of options for the future Main Street LRT alignment
- Aging water and wastewater infrastructure is at high risk of failure
- Construction is starting for interim replacement, until a decision on the LRT is finalized





How will traffic be managed?

- During construction on Queen Street, one lane of traffic will be maintained in each direction.
- During construction on Main Street, three lanes will be closed, and one lane of traffic maintained on Main Street South (northbound or southbound). This is being done for safety reasons and will decrease the duration by expediting the work. Traffic detours will be implemented.
- Paid duty police officers will assist with directing traffic while work is happening at intersections.
- Pedestrian access will generally be maintained to all businesses, and sidewalks will remain open.
 There will be some short-term works within the boulevards, followed by complete replacement of the curb and sidewalks, during which time pedestrians will be redirected to the other side of the street.

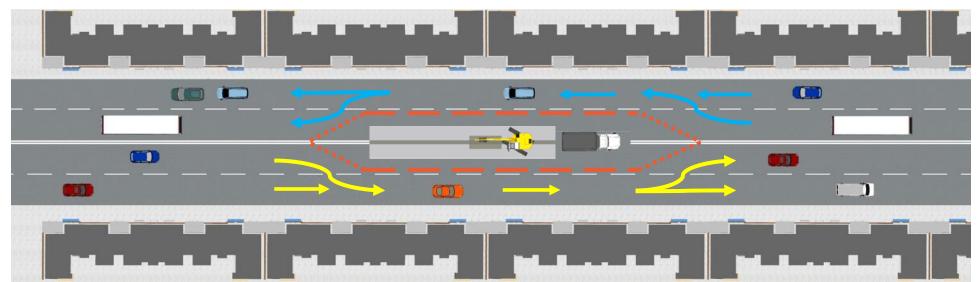





Minimizing Impacts during Construction

- The contractor will monitor noise and vibration levels both before and during construction to ensure that these are kept within acceptable levels.
- Any mud and dust created by construction will be controlled with street sweepers and water trucks.








Parking

- While works are being conducted within the road, on-street parking will not be possible within the area of active construction.
- Signage will be provided to direct vehicles to the nearest available parking garage.
- John Street parking garage will be unavailable until March 2022 due to repairs. A parking study has been conducted confirming that the other nearby garages within the downtown area have adequate space available.

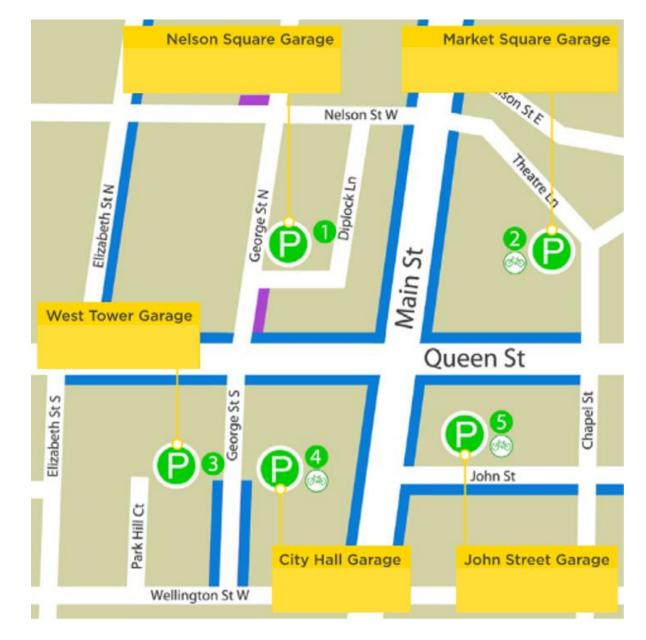






Deliveries

- While works are being conducted in front of businesses, deliveries and loading zones may be impacted.
- Since traffic will be reduced to maximum one lane with no passing lane, delivery vehicles will not be able to stop on the street within the active construction zone.
- Deliveries will need to be facilitated via side streets and adjacent laneways.

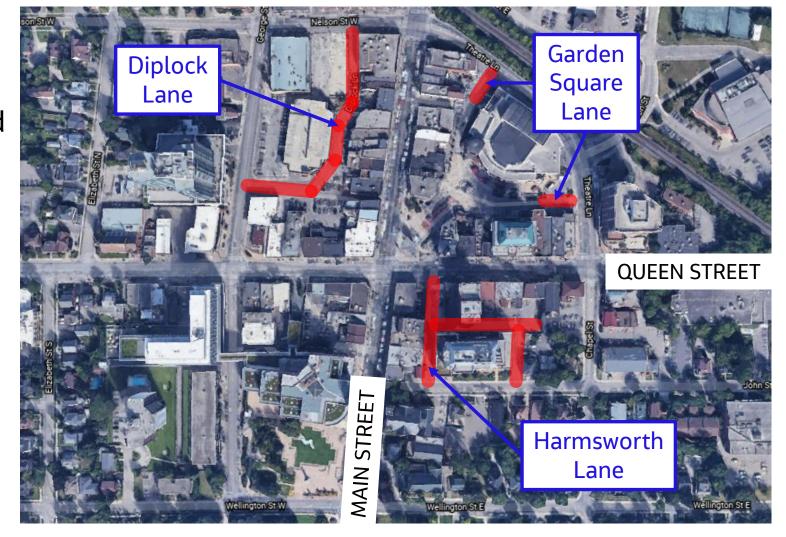


 Region of Peel project ambassador will be actively working with each business to facilitate deliveries (see final slide for ambassador contact information).







Stages of Construction

Stage 1: Underground watermain and sanitary sewer, which is generally installed in the middle of the road.




Stage 2: Installation of watermain and sewer connections to the houses and businesses on each side of the street.






Stage 3: Surface works for the roadway will be done for one half of the road at a time. Surface work for the sidewalk / boulevard will be completed at the same time as the roadworks.









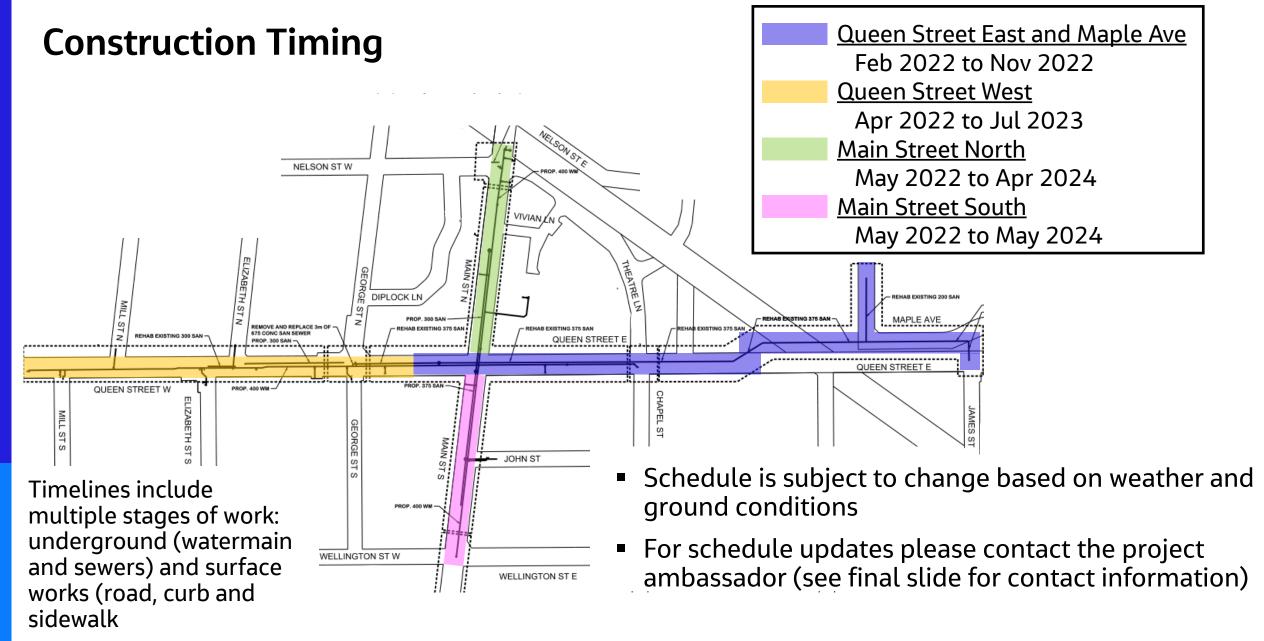





Construction Timing: Queen Street East* and Maple Avenue**


Preliminary schedule (subject to change based on weather and ground conditions):

- Stage 1 (middle of the road): Feb Apr 2022
- Stage 2A (north side): Apr May 2022
- Stage 2B (south side): May Jun 2022
- Stage 3A (south side road and sidewalk): Jun Aug 2022
- Stage 3B (north side road and sidewalk): Sep Nov 2022



**Maple Avenue work includes Stage 1 only



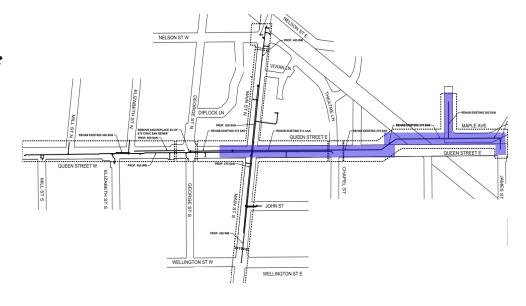




Construction Timing: Queen Street West

Preliminary schedule (subject to change based on weather and ground conditions):

- Stage 1 (middle of the road): Apr May 2022
- Stage 2A (north side): May Jul 2022
- Stage 2B (south side): Jul Sep 2022
- Stage 3A (south side road and sidewalk): Nov 2022 Apr 2023
- Stage 3B (north side road and sidewalk): Apr Jul 2023

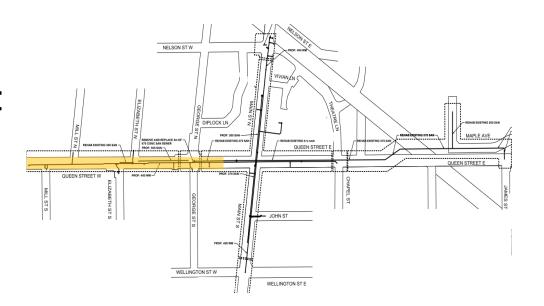




Construction Timing: Main Street North

Preliminary schedule (subject to change based on weather and ground conditions):


- Stage 1 (full road closure): May Dec 2022
- Stage 3A (west side road and sidewalk): Jul Sep 2023
- Stage 3B (east side road and sidewalk): Sep 2023 Apr 2024

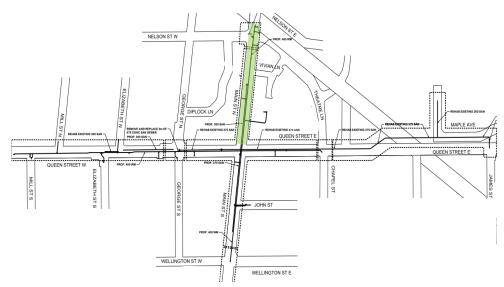




Construction Timing: Main Street South

Preliminary schedule (subject to change based on weather and ground conditions):



- Stage 2 (west side): Jan Feb 2023
- Stage 3A (west side road and sidewalk): Jul Sep 2023
- Stage 3B (east side road and sidewalk): Sep 2023 May 2024

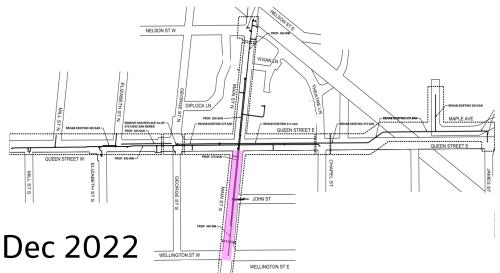

How to Stay Connected and Involved?

Please reach out to us with your comments and questions on this project.

The Project Team will post responses to questions received before January 14, 2022 on the Region's web-site peelregion.ca/construction/ on January 21, 2022





Avalon Myers

Project Ambassador 416-457-3889

Avalon.Myers@peelregion.ca

*Feedback collected on this project will conform with the *Freedom of Information and Protection of Privacy*Act. It will be documented as part of this project and may be publicly available.
